



CERTIFICATE OF TITLE 5 INSPECTION

Inspection requested by:

Name: Chris Stockman

Address: 475 Howard St

City, State & Zip: Northborough MA 01532-1032

Report preference: ☒ Email ☒ Mail

Inspection Location:

Street Address: 475 Howard St

City, State & Zip: Northborough MA 01532-1032

System Type: Tank/SAS System size: 1500

of Compartments 1 Filter: Yes

Date of Inspection: 10/24/2025

NOTE: This inspection report is valid for 3 years from the date of the inspection, if the tank is pumped annually.



Commonwealth of Massachusetts

Title 5 Official Inspection Form

Subsurface Sewage Disposal System Form - Not for Voluntary Assessments

Owner
information is
required for every
page.

475 Howard St

Property Address

Chris Stockman

Owner's Name

Northborough

City/Town

MA

State

01532-1

Zip Code

10/24/2025

Date of Inspection

Inspection results must be submitted on this form. Inspection forms may not be altered in any way. Please see completeness checklist at the end of the form.

Important: When filling out forms on the computer, use only the tab key to move your cursor - do not use the return key.



A. Inspector Information

Jason I. Gauthier

Name of Inspector

Northboro Septic Service, Inc. dba Curtis Septic

Company Name

124 Main Street

Company Address

Northboro

City/Town

(508) 393-7234

Telephone Number

MA

State

01532

Zip Code

SI4239

License Number

B. Certification

I certify that: **I am a DEP approved system inspector in full compliance with Section 15.340 of Title 5 (310 CMR 15.000);** I have personally inspected the sewage disposal system at the property address listed above; the information reported below is true, accurate and complete as of the time of my inspection; and the inspection was performed based on my training and experience in the proper function and maintenance of on-site sewage disposal systems. After conducting this inspection I have determined that the system:

- ☒ Passes
- ☐ Conditionally Passes
- ☐ Needs Further Evaluation by the Local Approving Authority
- ☐ Fails

10/24/2025

Date

The system inspector shall submit a copy of this inspection report to the Approving Authority (Board of Health or DEP) within 30 days of completing this inspection. If the system has a design flow of 10,000 gpd or greater, the inspector and the system owner shall submit the report to the appropriate regional office of the DEP. The original form should be sent to the system owner and copies sent to the buyer, if applicable, and the approving authority.

Please note: This report only describes conditions at the time of inspection and under the conditions of use at that time. This inspection does not address how the system will perform in the future under the same or different conditions of use.



Owner
information is
required for every
page.

Commonwealth of Massachusetts

Title 5 Official Inspection Form

Subsurface Sewage Disposal System Form - Not for Voluntary Assessments

475 Howard St

Property Address

Chris Stockman

Owner's Name

Northborough

MA

State

01532-1

Zip Code

10/24/2025

Date of Inspection

C. Inspection Summary

Inspection Summary: Complete 1, 2, 3, or 5 and all of 4 and 6.

1) System Passes:

☒ I have not found any information which indicates that any of the failure criteria described in 310 CMR 15.303 or in 310 CMR 15.304 exist. Any failure criteria not evaluated are indicated below.

Comments:

System appears to be functioning properly under its current usage. It is recommended that risers be installed on all 3 distribution boxes to bring the covers to within 6" of grade. As the design plan states the risers are required.

2) System Conditionally Passes:

☐ One or more system components as described in the "Conditional Pass" section need to be replaced or repaired. The system, upon completion of the replacement or repair, as approved by the Board of Health, will pass.

Check the box for "yes", "no" or "not determined" (Y, N, ND) for the following statements. If "not determined," please explain.

The septic tank is metal and over 20 years old* **or** the septic tank (whether metal or not) is structurally unsound, exhibits substantial infiltration or exfiltration or tank failure is imminent. System will pass inspection if the existing tank is replaced with a complying septic tank as approved by the Board of Health.

* A metal septic tank will pass inspection if it is structurally sound, not leaking and if a Certificate of Compliance indicating that the tank is less than 20 years old is available.

☐ Y ☐ N ☐ ND (Explain below):



Owner
information is
required for every
page.

Commonwealth of Massachusetts

Title 5 Official Inspection Form

Subsurface Sewage Disposal System Form - Not for Voluntary Assessments

475 Howard St

Property Address

Chris Stockman

Owner's Name

Northborough

MA

State

01532-1

Zip Code

10/24/2025

Date of Inspection

C. Inspection Summary (cont.)

2) System Conditionally Passes (cont.):

- ☐ Pump Chamber pumps/alarms not operational. System will pass with Board of Health approval if pumps/alarms are repaired.
- ☐ Observation of sewage backup or break out or high static water level in the distribution box due to broken or obstructed pipe(s) or due to a broken, settled or uneven distribution box. System will pass inspection if (with approval of Board of Health):
- | | | | |
|--|----------------------------|----------------------------|--|
| ☐ broken pipe(s) are replaced | ☐ Y | ☐ N | ☐ ND (Explain below): |
| ☐ obstruction is removed | ☐ Y | ☐ N | ☐ ND (Explain below): |
| ☐ distribution box is leveled or replaced | ☐ Y | ☐ N | ☐ ND (Explain below): |

- ☐ The system required pumping more than 4 times a year due to broken or obstructed pipe(s). The system will pass inspection if (with approval of the Board of Health):
- | | | | |
|--|----------------------------|----------------------------|--|
| ☐ broken pipe(s) are replaced | ☐ Y | ☐ N | ☐ ND (Explain below): |
| ☐ obstruction is removed | ☐ Y | ☐ N | ☐ ND (Explain below): |

3) Further Evaluation is Required by the Board of Health:

- ☐ Conditions exist which require further evaluation by the Board of Health in order to determine if the system is failing to protect public health, safety or the environment.

a. System will pass unless Board of Health determines in accordance with 310 CMR 15.303(1)(b) that the system is not functioning in a manner which will protect public health, safety and the environment:



Commonwealth of Massachusetts

Title 5 Official Inspection Form

Subsurface Sewage Disposal System Form - Not for Voluntary Assessments

475 Howard St

Property Address

Chris Stockman

Owner's Name

Northborough

City/Town

MA

State

01532-1

Zip Code

10/24/2025

Date of Inspection

Owner
information is
required for every
page.

C. Inspection Summary (cont.)

- ☐ Cesspool or privy is within 50 feet of a surface water
- ☐ Cesspool or privy is within 50 feet of a bordering vegetated wetland or a salt marsh

b. System will fail unless the Board of Health (and Public Water Supplier, if any) determines that the system is functioning in a manner that protects the public health, safety and environment:

- ☐ The system has a septic tank and soil absorption system (SAS) and the SAS is within 100 feet of a surface water supply or tributary to a surface water supply.
- ☐ The system has a septic tank and SAS and the SAS is within a Zone 1 of a public water supply.
- ☐ The system has a septic tank and SAS and the SAS is within 50 feet of a private water supply well.
- ☐ The system has a septic tank and SAS and the SAS is less than 100 feet but 50 feet or more from a private water supply well**.

Method used to determine distance: _____

** This system passes if the well water analysis, performed at a DEP certified laboratory, for fecal coliform bacteria indicates absent and the presence of ammonia nitrogen and nitrate nitrogen is equal to or less than 5 ppm, provided that no other failure criteria are triggered. A copy of the analysis must be attached to this form.

c. Other:

4) System Failure Criteria Applicable to All Systems:

You must indicate "Yes" or "No" to each of the following for all inspections:

Yes No

- | | | |
|--------------------------|-------------------------------------|---|
| ☐ | ☒ | Backup of sewage into facility or system component due to overloaded or clogged SAS or cesspool |
| ☐ | ☒ | Discharge or ponding of effluent to the surface of the ground or surface waters due to an overloaded or clogged SAS or cesspool |



Commonwealth of Massachusetts

Title 5 Official Inspection Form

Subsurface Sewage Disposal System Form - Not for Voluntary Assessments

475 Howard St

Property Address

Chris Stockman

Owner's Name

Northborough

City/Town

MA

State

01532-1

Zip Code

10/24/2025

Date of Inspection

Owner
information is
required for every
page.

C. Inspection Summary (cont.)

4) System Failure Criteria Applicable to All Systems: (cont.)

Yes No

☐☒

Static liquid level in the distribution box above outlet invert due to an overloaded or clogged SAS or cesspool

☐☒

Liquid depth in cesspool is less than 6" below invert or available volume is less than ½ day flow

☐☒

Required pumping more than 4 times in the last year **NOT** due to clogged or obstructed pipe(s). Number of times pumped: _____.

☐☒

Any portion of the SAS, cesspool or privy is below high ground water elevation.

☐☒

Any portion of cesspool or privy is within 100 feet of a surface water supply or tributary to a surface water supply.

☐☒

Any portion of a cesspool or privy is within a Zone 1 of a public water supply well.

☐☒

Any portion of a cesspool or privy is within 50 feet of a private water supply well.

☐☒

Any portion of a cesspool or privy is less than 100 feet but greater than 50 feet from a private water supply well with no acceptable water quality analysis. **[This system passes if the well water analysis, performed at a DEP certified laboratory, for fecal coliform bacteria indicates absent and the presence of ammonia nitrogen and nitrate nitrogen is equal to or less than 5 ppm, provided that no other failure criteria are triggered. A copy of the analysis and chain of custody must be attached to this form.]**

☐☒

The system is a cesspool serving a facility with a design flow of 2000 gpd-10,000 gpd.

☐☒

The system fails. I have determined that one or more of the above failure criteria exist as described in 310 CMR 15.303, therefore the system fails. The system owner should contact the Board of Health to determine what will be necessary to correct the failure.

5) Large Systems: To be considered a large system the system must serve a facility with a design flow of 10,000 gpd to 15,000 gpd.

For large systems, you must indicate either "yes" or "no" to each of the following, in addition to the questions in Section C.4.

Yes No

☐☐

the system is within 400 feet of a surface drinking water supply

☐☐

the system is within 200 feet of a tributary to a surface drinking water supply

☐☐

the system is located in a nitrogen sensitive area (Interim Wellhead Protection Area – IWPA) or a mapped Zone II of a public water supply well



Owner
information is
required for every
page.

Commonwealth of Massachusetts

Title 5 Official Inspection Form

Subsurface Sewage Disposal System Form - Not for Voluntary Assessments

475 Howard St

Property Address

Chris Stockman

Owner's Name

Northborough

City/Town

MA

State

01532-1

Zip Code

10/24/2025

Date of Inspection

C. Inspection Summary (cont.)

If you have answered "yes" to any question in Section C.5 the system is considered a significant threat, or answered "yes" to any question in Section C.4 above the large system has failed. The owner or operator of any large system considered a significant threat under Section C.5 or failed under Section C.4 shall upgrade the system in accordance with 310 CMR 15.304. The system owner should contact the appropriate regional office of the Department.

6. You must indicate "yes" or "no" for each of the following for *all* inspections:

Yes No



Pumping information was provided by the owner, occupant, or Board of Health



Were any of the system components pumped out in the previous two weeks?



Has the system received normal flows in the previous two week period?



Have large volumes of water been introduced to the system recently or as part of this inspection?



Were as built plans of the system obtained and examined? (If they were not available note as N/A)



Was the facility or dwelling inspected for signs of sewage back up?



Was the site inspected for signs of break out?



Were all system components, excluding the SAS, located on site?



Were the septic tank manholes uncovered, opened, and the interior of the tank inspected for the condition of the baffles or tees, material of construction, dimensions, depth of liquid, depth of sludge and depth of scum?



Was the facility owner (and occupants if different from owner) provided with information on the proper maintenance of subsurface sewage disposal systems? The **size and location of the Soil Absorption System (SAS)** on the site has been determined based on:



Existing information. For example, a plan at the Board of Health.



Determined in the field (if any of the failure criteria related to Part C is at issue approximation of distance is unacceptable) [310 CMR 15.302(5)]



Commonwealth of Massachusetts

Title 5 Official Inspection Form

Subsurface Sewage Disposal System Form - Not for Voluntary Assessments

475 Howard St

Property Address

Chris Stockman

Owner's Name

Northborough

City/Town

MA

State

01532-1

Zip Code

10/24/2025

Date of Inspection

Owner
information is
required for every
page.

D. System Information

1. Residential Flow Conditions:

Number of bedrooms (design): 4 Number of bedrooms (actual): 4

DESIGN flow based on 310 CMR 15.203 (for example: 110 gpd x # of bedrooms): 440

Description:

1500 gallon septic tank with filter/3 distribution boxes, soil absorption system

Number of current residents: 2

Does residence have a garbage grinder? ☐ Yes ☒ No

Does residence have a water treatment unit? ☐ Yes ☒ No

If yes, discharges to: _____

Is laundry on a separate sewage system? (Include laundry system inspection information in this report.) ☐ Yes ☒ No

Laundry system inspected? ☐ Yes ☒ No

Seasonal use? ☐ Yes ☒ No

Water meter readings, if available (last 2 years usage (gpd)): Private Well

Detail:

Well is 100'c to the SAS

Sump pump? ☐ Yes ☒ No

Last date of occupancy: Current
Date



Owner
information is
required for every
page.

Commonwealth of Massachusetts

Title 5 Official Inspection Form

Subsurface Sewage Disposal System Form - Not for Voluntary Assessments

475 Howard St

Property Address

Chris Stockman

Owner's Name

Northborough

City/Town

MA

State

01532-1

Zip Code

10/24/2025

Date of Inspection

D. System Information (cont.)

2. Commercial/Industrial Flow Conditions:

Type of Establishment:

Design flow (based on 310 CMR 15.203):

Gallons per day (gpd)

Basis of design flow (seats/persons/sq.ft., etc.):

Grease trap present?

☐ Yes ☐ No

Water treatment unit present?

☐ Yes ☐ No

If yes, discharges to:

Industrial waste holding tank present?

☐ Yes ☐ No

Non-sanitary waste discharged to the Title 5 system?

☐ Yes ☐ No

Water meter readings, if available:

Last date of occupancy/use:

Date

Other (describe below):

3. Pumping Records:

Source of information:

Last pumped by Curtis Septic on 6/24/24

Was system pumped as part of the inspection?

☐ Yes ☒ No

If yes, volume pumped:

gallons

How was quantity pumped determined?

Reason for pumping:



Commonwealth of Massachusetts

Title 5 Official Inspection Form

Subsurface Sewage Disposal System Form - Not for Voluntary Assessments

475 Howard St

Property Address

Chris Stockman

Owner's Name

Northborough

City/Town

MA

State

01532-1

Zip Code

10/24/2025

Date of Inspection

Owner
information is
required for every
page.

D. System Information (cont.)

4. Type of System:

- ☐ Septic tank, distribution box, soil absorption system
- ☐ Single cesspool
- ☐ Overflow cesspool
- ☐ Privy
- ☐ Shared system (yes or no) (if yes, attach previous inspection records, if any)
- ☐ Innovative/Alternative technology. Attach a copy of the current operation and maintenance contract (to be obtained from system owner) and a copy of latest inspection of the I/A system by system operator under contract
- ☐ Tight tank. Attach a copy of the DEP approval.
- ☒ Other (describe):
Septic tank, 3 distribution boxes, soil absorption system

Approximate age of all components, date installed (if known) and source of information:

Installed 9/3/04 per as built plan

Were sewage odors detected when arriving at the site?

☐ Yes ☒ No

5. Building Sewer (locate on site plan):

Depth below grade:

7' Below Sill

feet

Material of construction:

☐ cast iron

☐ 40 PVC

☒ other (explain):

4" ABS

Distance from private water supply well or suction line:

50'+ to the well

feet

Comments (on condition of joints, venting, evidence of leakage, etc.):

All visible joints are of good condition with no evidence of any leakage. Appears to be vented properly.



Commonwealth of Massachusetts

Title 5 Official Inspection Form

Subsurface Sewage Disposal System Form - Not for Voluntary Assessments

475 Howard St

Property Address

Chris Stockman

Owner's Name

Northborough

City/Town

MA

State

01532-1

Zip Code

10/24/2025

Date of Inspection

Owner
information is
required for every
page.

D. System Information (cont.)

6. Septic Tank (locate on site plan):

21" with risers on inlet and outlet to 6" of grade

Depth below grade:

feet

Material of construction:

☒ concrete

☐ metal

☐ fiberglass

☐ polyethylene

☐ other (explain)

If tank is metal, list age:

years

Is age confirmed by a Certificate of Compliance? (attach a copy of certificate)

☐ Yes

☐ No

Dimensions:

10'6"L x 5'8"W 5'D

2"

Sludge depth:

32"

Distance from top of sludge to bottom of outlet tee or baffle

0"

Scum thickness

6"

Distance from top of scum to top of outlet tee or baffle

14"

Distance from bottom of scum to bottom of outlet tee or baffle

Visual Inspection

How were dimensions determined?

Comments (on pumping recommendations, inlet and outlet tee or baffle condition, structural integrity, liquid levels as related to outlet invert, evidence of leakage, etc.):

Recommend yearly pumping, tank is a 1500 gallon tank. Inlet and outlet tees are PVC and of good working condition. Outlet tee has an effluent filter that should be cleaned yearly. Tank is structurally sound with no evidence of any leakage. Liquid level is at the base of the outlet invert.



Commonwealth of Massachusetts

Title 5 Official Inspection Form

Subsurface Sewage Disposal System Form - Not for Voluntary Assessments

475 Howard St

Property Address

Chris Stockman

Owner's Name

Northborough

City/Town

MA

State

01532-1

Zip Code

10/24/2025

Date of Inspection

Owner
information is
required for every
page.

D. System Information (cont.)

7. Grease Trap (locate on site plan):

Depth below grade:

feet

Material of construction:

☐ concrete

☐ metal

☐ fiberglass

☐ polyethylene

☐ other (explain):

Dimensions:

Scum thickness

Distance from top of scum to top of outlet tee or baffle

Distance from bottom of scum to bottom of outlet tee or baffle

Date of last pumping:

Date

Comments (on pumping recommendations, inlet and outlet tee or baffle condition, structural integrity, liquid levels as related to outlet invert, evidence of leakage, etc.):

8. Tight or Holding Tank (tank must be pumped at time of inspection) (locate on site plan):

Depth below grade:

Material of construction:

☐ concrete

☐ metal

☐ fiberglass

☐ polyethylene

☐ other (explain):

Dimensions:

Capacity:

gallons

Design Flow:

gallons per day



Commonwealth of Massachusetts

Title 5 Official Inspection Form

Subsurface Sewage Disposal System Form - Not for Voluntary Assessments

475 Howard St

Property Address

Chris Stockman

Owner's Name

Northborough

City/Town

MA

State

01532-1

Zip Code

10/24/2025

Date of Inspection

Owner
information is
required for every
page.

D. System Information (cont.)

8. Tight or Holding Tank (cont.)

Alarm present:

☐ Yes

☐ No

Alarm level: _____

Alarm in working order:

☐ Yes

☐ No

Date of last pumping:

Date

Comments (condition of alarm and float switches, etc.):

* Attach copy of current pumping contract (required). Is copy attached?

☐ Yes

☐ No

9. Distribution Box (if present must be opened) (locate on site plan):

0" - 0" - 0"

Depth of liquid level above outlet invert _____

Comments (note if box is level and distribution to outlets equal, any evidence of solids carryover, any evidence of leakage into or out of box, etc.):

There are 3 distribution boxes. Box #1 and Box #2 are velocity reducing boxes. They have one inlet and 1 outlet that are of good working condition. Box #3 is level with equal distribution to all 3 outlets. No evidence of any solids carryover in any box. No evidence of any leakage in to or out of any of the boxes. Boxes are all 7 outlet boxes. Box 1 and box 2 are 28" below grade. Box 3 is 26" below grade. It is recommended that risers be installed on all boxes to bring the covers to within 6" of grade as the design plan states that risers are required.



Commonwealth of Massachusetts

Title 5 Official Inspection Form

Subsurface Sewage Disposal System Form - Not for Voluntary Assessments

475 Howard St

Property Address

Chris Stockman

Owner's Name

Northborough

MA

State

01532-1

Zip Code

10/24/2025

Date of Inspection

Owner
information is
required for every
page.

D. System Information (cont.)

10. Pump Chamber (locate on site plan):

Pumps in working order:

☐ Yes

☐ No*

Alarms in working order:

☐ Yes

☐ No*

Comments (note condition of pump chamber, condition of pumps and appurtenances, etc.):

* If pumps or alarms are not in working order, system is a conditional pass.

11. Soil Absorption System (SAS) (locate on site plan, excavation not required):

If SAS not located, explain why:

Type:

☐

leaching pits

number:

☐

leaching chambers

number:

☐

leaching galleries

number:

3 @ 44'L per plan

☒

leaching trenches

number, length:

☐

leaching fields

number, dimensions:

☐

overflow cesspool

number:

☐

innovative/alternative system

Type/name of technology:



Commonwealth of Massachusetts

Title 5 Official Inspection Form

Subsurface Sewage Disposal System Form - Not for Voluntary Assessments

475 Howard St

Property Address

Chris Stockman

Owner's Name

Northborough

City/Town

MA

State

01532-1

Zip Code

10/24/2025

Date of Inspection

Owner
information is
required for every
page.

D. System Information (cont.)

11. Soil Absorption System (SAS) (cont.)

Comments (note condition of soil, signs of hydraulic failure, level of ponding, damp soil, condition of vegetation, etc.):

Dry gravel soil with no signs of any hydraulic failure. No ponding . Normal grass vegetation.

12. Cesspools (cesspool must be pumped as part of inspection) (locate on site plan):

Number and configuration

Depth – top of liquid to inlet invert

Depth of solids layer

Depth of scum layer

Dimensions of cesspool

Materials of construction

Indication of groundwater inflow

☐ Yes

☐ No

Comments (note condition of soil, signs of hydraulic failure, level of ponding, condition of vegetation, etc.):



Commonwealth of Massachusetts

Title 5 Official Inspection Form

Subsurface Sewage Disposal System Form - Not for Voluntary Assessments

475 Howard St

Property Address

Chris Stockman

Owner's Name

Northborough

City/Town

MA

State

01532-1

Zip Code

10/24/2025

Date of Inspection

Owner
information is
required for every
page.

D. System Information (cont.)

13. **Privy** (locate on site plan):

Materials of construction:

Dimensions

Depth of solids

Comments (note condition of soil, signs of hydraulic failure, level of ponding, condition of vegetation, etc.):



Commonwealth of Massachusetts

Title 5 Official Inspection Form

Subsurface Sewage Disposal System Form - Not for Voluntary Assessments

475 Howard St

Property Address

Chris Stockman

Owner's Name

Northborough

City/Town

MA

State

01532-1

Zip Code

10/24/2025

Date of Inspection

Owner
information is
required for every
page.

D. System Information (cont.)

14. Sketch Of Sewage Disposal System:

Provide a view of the sewage disposal system, including ties to at least two permanent reference landmarks or benchmarks. Locate all wells within 100 feet. Locate where public water supply enters the building. Check one of the boxes below:

- ☒ hand-sketch in the area below
☐ drawing attached separately

AS-BUILT

CURTIS SEPTIC SERVICE

Date: _____ Service Rep: Jay #33

JOB TYPE:

☐ D-Box ☐ Pipe ☐ Tank ☐ New System ☐ Sewer Line ☐ Pump ☒ T5 Inspection

☐ Other _____

(NOT TO SCALE)

Depths		A	B	C	D
6" to 15" K	Tank Inlet	10'	25"		
6" to 15" K	Tank Outlet	18"	19"		
28"	D-Box #1	39'	41'		
28"	D-Box #2	73"	67"		
26"	D-Box #3	74"	68"		

Customer Name: _____

Address: 475 Howard St.

Northboro

Mailing Address: _____



Commonwealth of Massachusetts

Title 5 Official Inspection Form

Subsurface Sewage Disposal System Form - Not for Voluntary Assessments

475 Howard St

Property Address

Chris Stockman

Owner's Name

Northborough

City/Town

MA

State

01532-1

Zip Code

10/24/2025

Date of Inspection

Owner
information is
required for every
page.

D. System Information (cont.)

15. Site Exam:

☒ Check Slope

☒ Surface water

☒ Check cellar

☒ Shallow wells

Estimated depth to high ground water:

92"+
feet

Please indicate all methods used to determine the high ground water elevation:

☒ Obtained from system design plans on record

If checked, date of design plan reviewed:

9/12/03
Date

☐ Observed site (abutting property/observation hole within 150 feet of SAS)

☐ Checked with local Board of Health - explain:

☐ Checked with local excavators, installers - (attach documentation)

☐ Accessed USGS database - explain:

You **must** describe how you established the high ground water elevation:

Soil testing info dated 5/27/03 on design plan dated 9/12/03 lists no mottles to 92" and 94".

Before filing this Inspection Report, please see Report Completeness Checklist on next page.



Owner
information is
required for every
page.

Commonwealth of Massachusetts

Title 5 Official Inspection Form

Subsurface Sewage Disposal System Form - Not for Voluntary Assessments

475 Howard St

Property Address

Chris Stockman

Owner's Name

Northborough

City/Town

MA

State

01532-1

Zip Code

10/24/2025

Date of Inspection

E. Report Completeness Checklist

Complete all applicable sections of this form inclusive of:

☒ A. Inspector Information: Complete all fields in this section.

☒ B. Certification: Signed & Dated and 1, 2, 3, or 4 checked

☒ C. Inspection Summary:

1, 2, 3, or 5 completed as appropriate

4 (Failure Criteria) and 6 (Checklist) completed

☒ D. System Information:

For 8: Tight/Holding Tank – Pumping contract attached

For 15: Sketch of Sewage Disposal System drawn on pg. 16 or attached

For 16: Explanation of estimated depth to high groundwater included

CURTIS

SEPTIC SERVICE

Title 5 Inspection
475 Howard Street
Northborough, MA 01532
Address: Inspection Date: 10/24/25

House



Stow • 128 Great Rd • (978) 897-3600 •
Northboro • 124 Main St • (508) 393-7234 •
Littleton • 6 Meeting House Rd • (978) 540-5555 •
Info@curtis-septic.com

CURTIS

SEPTIC SERVICE

Title 5 Inspection
475 Howard Street
Northborough, MA 01532
Address: Inspection Date: 10/24/25

Plumbing



Stow • 128 Great Rd • (978) 897-3600 •
Northboro • 124 Main St • (508) 393-7234 •
Littleton • 6 Meeting House Rd • (978) 540-5555 •
Info@curtisseptic.com

CURTIS

SEPTIC SERVICE

Title 5 Inspection
475 Howard Street
Northborough, MA 01532
Address: Inspection Date: 10/24/25

Inlet tee



Stow • 128 Great Rd • (978) 897-3600 •
Northboro • 124 Main St • (508) 393-7234 •
Littleton • 6 Meeting House Rd • (978) 540-5555 •
Info@curtisseptic.com

CURTIS

SEPTIC SERVICE

Title 5 Inspection
475 Howard Street
Northborough, MA 01532
Address: Inspection Date: 10/24/25

Outlet tee with filter



Stow • 128 Great Rd • (978) 897-3600 •
Northboro • 124 Main St • (508) 393-7234 •
Littleton • 6 Meeting House Rd • (978) 540-5555 •
Info@curtisseptic.com

CURTIS

SEPTIC SERVICE

Title 5 Inspection
475 Howard Street
Northborough, MA 01532
Address: Inspection Date: 10/24/25

Distribution Box #1



Stow • 128 Great Rd • (978) 897-3600 •
Northboro • 124 Main St • (508) 393-7234 •
Littleton • 6 Meeting House Rd • (978) 540-5555 •
Info@curtis-septic.com

CURTIS

SEPTIC SERVICE

Title 5 Inspection
475 Howard Street
Northborough, MA 01532
Address: Inspection Date: 10/24/25

Distribution Box #2



Stow • 128 Great Rd • (978) 897-3600 •
Northboro • 124 Main St • (508) 393-7234 •
Littleton • 6 Meeting House Rd • (978) 540-5555 •
Info@curtisseptic.com

CURTIS

SEPTIC SERVICE

Title 5 Inspection
475 Howard Street
Northborough, MA 01532
Address: Inspection Date: 10/24/25

Distribution Box 3



Stow • 128 Great Rd • (978) 897-3600 •
Northboro • 124 Main St • (508) 393-7234 •
Littleton • 6 Meeting House Rd • (978) 540-5555 •
Info@curtis Septic.com



CURTIS

SEPTIC SERVICE

Title 5 Inspection
 475 Howard Street
 Northborough, MA 01532
 Address: Inspection Date: 10/24/25

As built Elevations
 and Ties


SCHEDULE OF ELEVATIONS		PROP.	EXIST.
INVERT AT FOUNDATION		124.5	126.24
INVERT AT TANK IN		124.0	125.87
INVERT AT TANK OUT		123.8	125.50
INVERT AT D-BOX#1 IN		116.0	112.76
INVERT AT D-BOX #1OUT		115.8	112.51
INVERT AT D-BOX#2 IN		103.5	103.49
INVERT AT D-BOX#2 OUT		103.3	103.30
INVERT AT D-BOX#3 IN		103.1	103.19
INVERT AT D-BOX#3 OUT		102.9	102.99
BEGINNING	L-1	102.7	102.97
	L-2	101.7	101.75
	L-3	99.7	101.71
	L-1	102.5	102.74
	L-2	101.5	101.56
	L-3	99.5	101.49
	END		
SCHEDULE OF SYS. TIES		COR.A	COR.B
END TANK COVER		22.8'	36.5'
END TANK COVER		28.2'	29.5'
CENTER "D"-BOX		51.9'	36.7'
CENTER "D"-BOX		92.7'	62.9'
CENTER "D"-BOX		95.0'	63.8'
BEGINNING	L-1	96.6'	63.9'
	L-2	110.0'	79.6'
	L-3	127.2'	81.9'
END	L-1	127.2'	81.9'
	L-3	137.5'	94.4'

CURTIS

SEPTIC SERVICE

Title 5 Inspection
475 Howard Street
Northborough, MA 01532
Address: Inspection Date: 10/24/25

As built

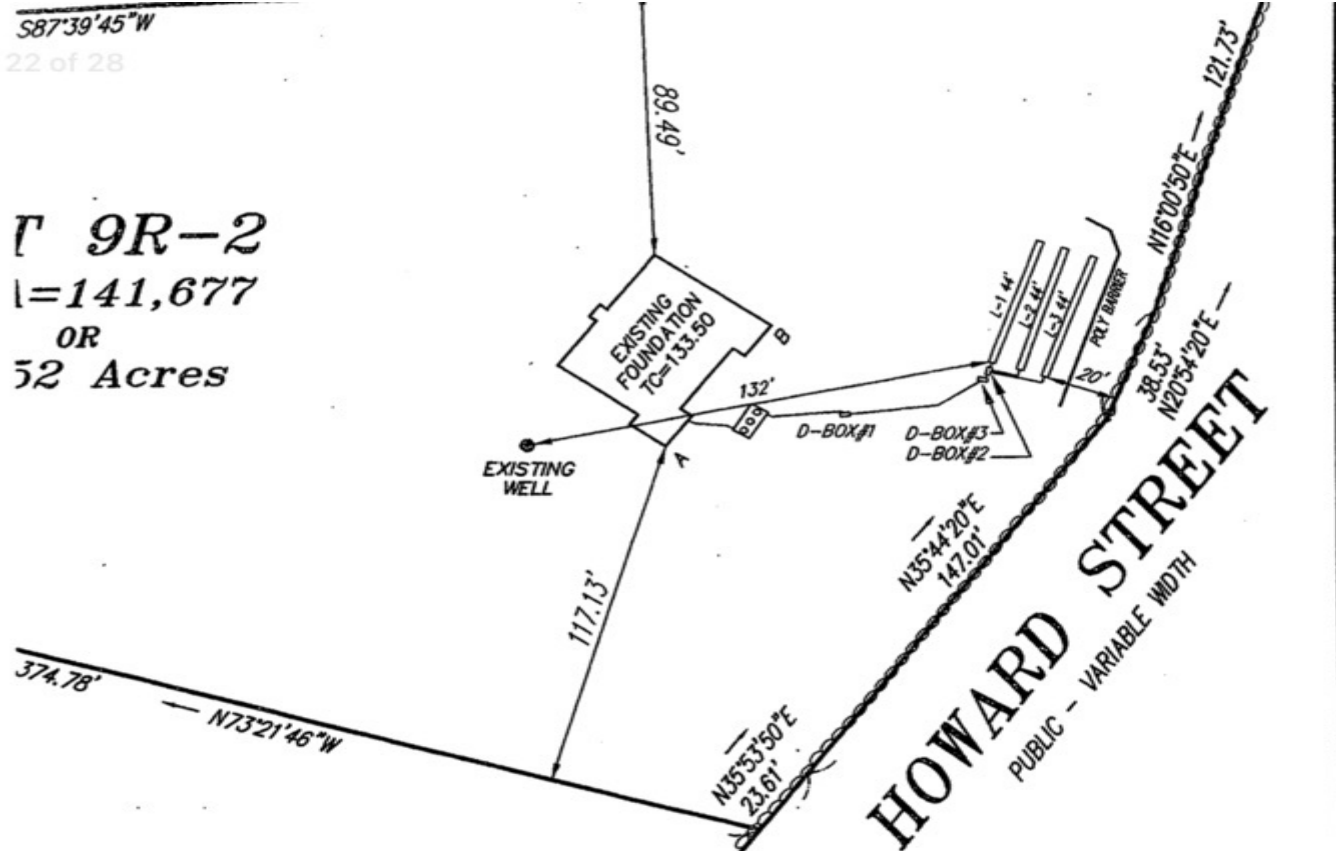

PREPARED FOR:
KARL NYE

DATE: SEPT. 3, 2004 SCALE: 1"=50'

AS-BUILT SEPTIC PLAN
#475
LOT 9R-2 HOWARD STREET

NORTHBOROUGH, MA.

CONNORSTONE
CONSULTING CIVIL ENGINEERS
AND LAND SURVEYORS
276 WEST MAIN STREET
NORTHBOROUGH, MASSACHUSETTS 01532

IEREON
CODE
REGULATIONS.
10' TO SYSTEM.



SEPTIC SERVICE

Title 5 Inspection
475 Howard Street
Northborough, MA 01532
Address: Inspection Date: 10/24/25

Design Info.

GENERAL NOTES

1. ALL CONSTRUCTION TO CONFORM TO THE REQUIREMENTS OF THE MASSACHUSETTS ENVIRONMENTAL CODE, TITLE FIVE, AND THE TOWN OF NORTHBOROUGH BOARD OF HEALTH REGULATIONS.

2. SOIL TESTING PERFORMED IN ACCORDANCE WITH THE INSTRUCTIONS OF MASSACHUSETTS ENVIRONMENTAL CODE, TITLE FIVE.

3. ESTIMATED FLOW = 4 BDRMS X 110 GPD/BR = 440 GPD

4. DESIGN PERCOLATION RATE = 15.0 MPI

5. LEACHING AREA CALCULATION =

$$\begin{aligned} SA &= 6(2' \times 44') = 528 \text{ SF} \\ BA &= 3(2' \times 44') = 264 \text{ SF} > 792 \text{ SF}(0.56 \text{ GPD/SF}) = 443 \text{ GPD} \end{aligned}$$

6. LEACHING LINES SHALL CONSIST OF PERFORATED P.V.C. PIPE.

7. THERE ARE NO SURFACE WATER SUPPLIES OR WETLANDS BORDERING SURFACE WATER SUPPLIES OR PUBLIC WELLS WITHIN 400' OF SITE.

8. THERE ARE NO PRIVATE WELLS WITHIN 200' OF SITE.

9. THERE ARE NO BORDERING VEGETATED WETLANDS, INLAND BANKS, OR SURFACE WATERS WITHIN 100' OF SYSTEM.

10. THERE ARE NO SURFACE OR SUBSURFACE DRAINS WHICH ARE USED TO LOWER THE GROUND WATER.

11. THERE ARE NO VERNAL POOLS WITHIN 100' OF SITE.

12. SITE NOT WITHIN 100 YEAR FLOOD PLAIN.

13. EFFLUENT BEING DISCHARGED TO SYSTEM CAN BE ASSOCIATED WITH RESIDENTIAL USE ONLY.

14. ALL ELEVATIONS REFER TO T.B.M TBM POLE-#7
NAIL EL.=101.46

15. FOR PROPER PERFORMANCE, SEPTIC TANK SHOULD BE PUMPED ANNUALLY.

16. NOTES

DO NOT APPLY.

CURTIS

SEPTIC SERVICE

Title 5 Inspection
 475 Howard Street
 Northborough, MA 01532
 Address: Inspection Date: 10/24/25

Plan

<u>APPLICANT</u>		<u>LOCATION</u>	
KARL NYE		LOT 9R-2 HOWARD STREET NORTHBOROUGH, MA. #467	
	NO.	DATE:	REVISION:
	CONNORSTONE CONSULTING CIVIL ENGINEERS AND LAND SURVEYORS 276 WEST MAIN STREET NORTHBOROUGH, MASSACHUSETTS 01532		
	PROPOSED SEWAGE DISPOSAL SYSTEM		
DATE: 09--12-03		SHEET 1 OF 2	

SEPTIC SERVICE

Title 5 Inspection
475 Howard Street
Northborough, MA 01532
Address: Inspection Date: 10/24/25

Proposed elevations

SCHEDULE OF ELEVATIONS


TOP OF FOUNDATION T.C. =	132.0		
BASEMENT FLOOR FIN. C.F. =	124.0		
INVERT OF PIPE AT FOUNDATION =	124.5		
INVERT AT SEPTIC TANK INLET =	124.0		
INVERT AT SEPTIC TANK OUTLET =	123.8		
INVERT AT DISTRIBUTION BOX #1 INLET =	116.0		
INVERT AT DISTRIBUTION BOX #1 OUTLET =	115.8		
INVERT AT DISTRIBUTION BOX #2 INLET =	103.5		
INVERT AT DISTRIBUTION BOX #2 OUTLET =	103.3		
INVERT AT DISTRIBUTION BOX #3 INLET =	103.1		
INVERT AT DISTRIBUTION BOX #3 OUTLET =	102.9		
	L-1	L-2	L-3
INVERT AT LEACHING LINES (BEGINNING) =	102.7	101.7	99.7
INVERT AT LEACHING LINES (END) =	102.5	101.5	99.5
ELEVATION OF TRENCH BOTTOM =	100.5	99.5	97.5
FINISH GRADE OVER LEACHING AREA (F.G.) =	104-102		

CURTIS

SEPTIC SERVICE

Title 5 Inspection
475 Howard Street
Northborough, MA 01532
Address: Inspection Date: 10/24/25

Proposed layout

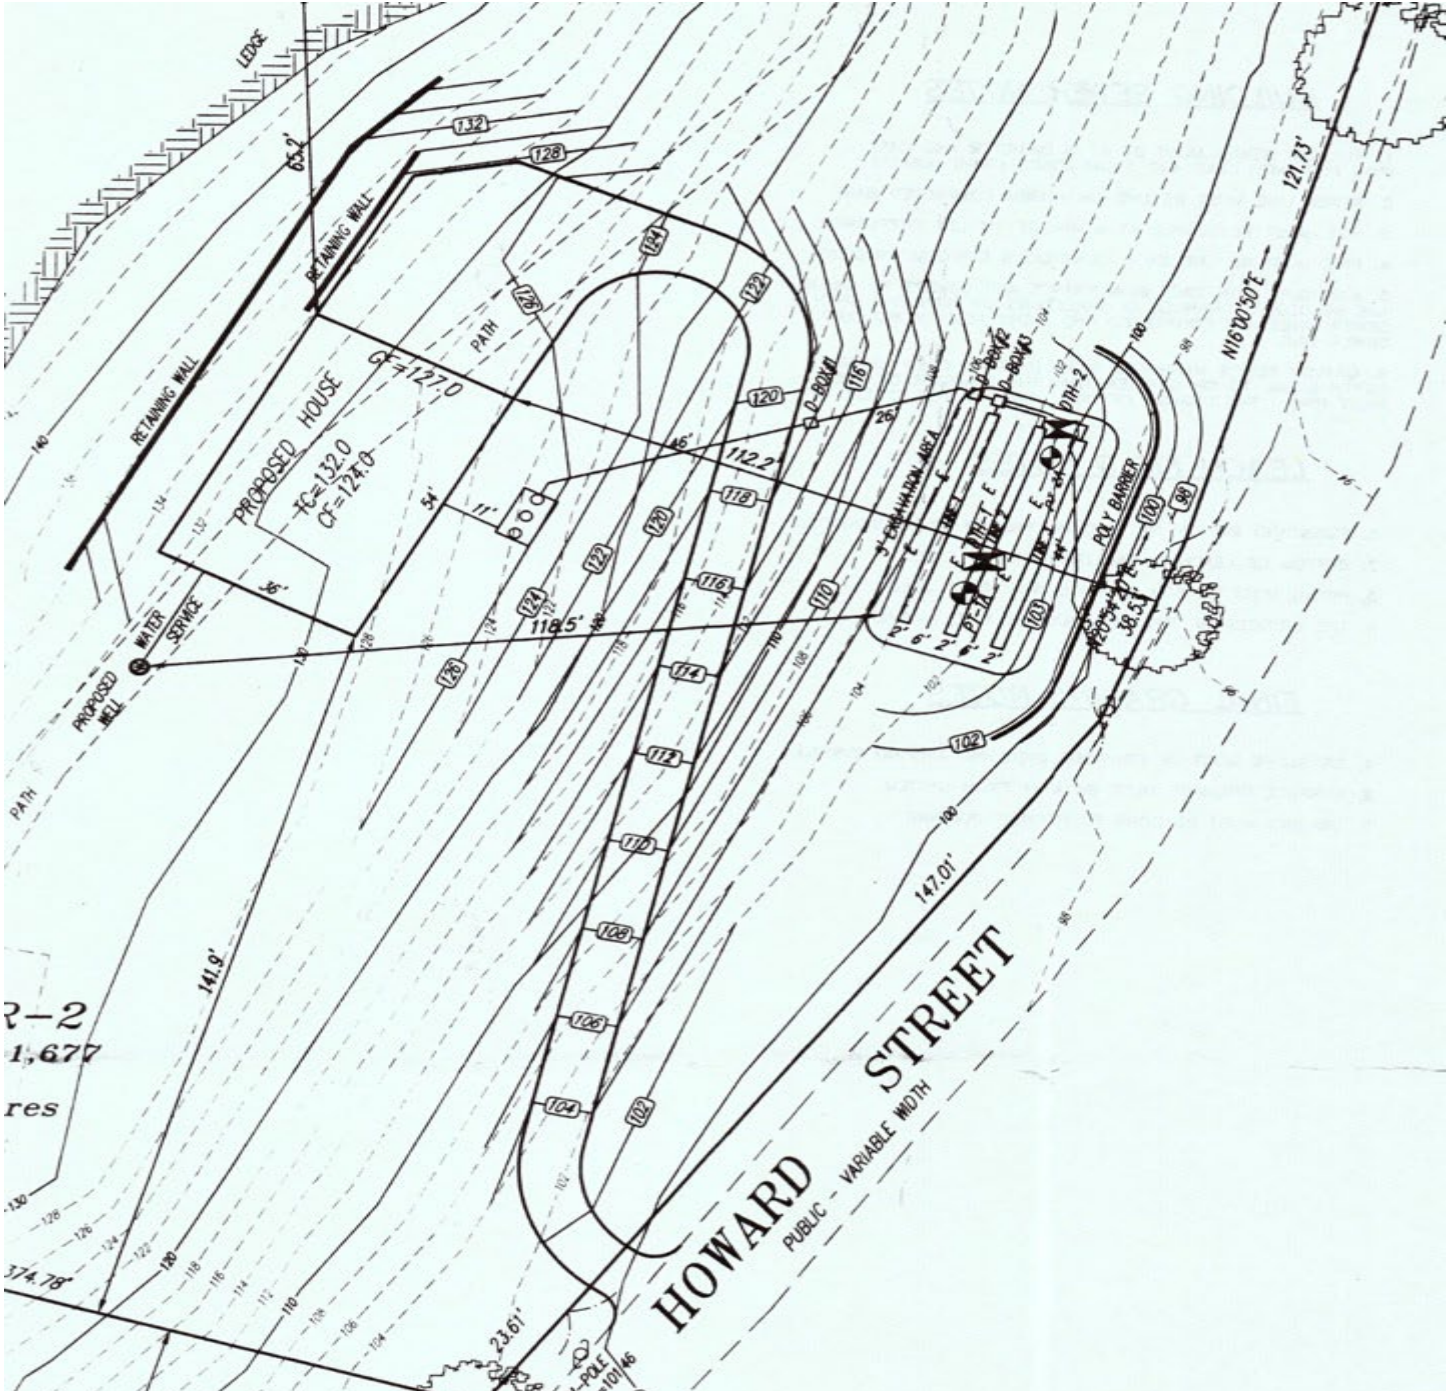

Stow • 128 Great Rd • (978) 897-3600 •
Northboro • 124 Main St • (508) 393-7234 •
Littleton • 6 Meeting House Rd • (978) 540-5555 •
Info@curtis-septic.com

CURTIS SEPTIC SERVICE

Title 5 Inspection
475 Howard Street
Northborough, MA 01532
Address: Inspection Date: 10/24/25

Soil test Info.

SOIL LOGS		SOIL TEST RESULTS	
NO. DTH-1 102.0 ELEV.	NO. DTH-2 101.0 ELEV.		
0-8 Ap SANDY LOAM 10YR 3/2 8-30 Bw LOAMY SAND 10YR 6/6 30-94 C SANDY LOAM 10YR 5/4	0-10 Ap SANDY LOAM 10YR 3/2 10-36 Bw LOAMY SAND 10YR 6/6 36-92 C SANDY LOAM 10YR 5/4		
NO WATER & NO MOTTLES OBSERVED S.H.G.W. ELEV. = 94.2	NO WATER & NO MOTTLES OBSERVED S.H.G.W. ELEV. = 93.3		
NO. ELEV.	NO. ELEV.		
DATE: 5/27/03			
SOIL EVALUATOR: MIKE SULLIVAN			
B.O.H. INSPECTOR: JACK WALLACE			

CURTIS

SEPTIC SERVICE

Title 5 Inspection
475 Howard Street
Northborough, MA 01532
Address: Inspection Date: 10/24/25

System Profile

PROFILE OF SYSTEM

NOT TO SCALE

